Figure 5
Island Complex Murray Road, and Harvard Road North Sites
Remedial Design Schedule

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Spokane River Metals Sites Planning**	**82 days**	**Mon 3/21/06**	**Tue 12/12/06**	
6	**Island Complex Remedial Design and Remedial Action**	**289 days**	**Tue 9/12/06**	**Fri 10/19/07**	
	Island Complex Remedial Design	**203 days**	**Tue 9/12/06**	**Thu 6/21/07**	
	Submit 30% Design Package	12 days	Tue 9/12/06	Wed 9/27/06	3
9	Review of 30% Design Package	55 days	Thu 9/28/06	Wed 12/13/06	8
10	Prepare Draft 90% Design Package	30 days	Thu 12/14/06	Wed 1/24/07	9
11	Review & Comment - 90% Design Package	10 days	Thu 1/25/07	Wed 2/7/07	10
12	Prepare Final 90% Design Package	10 days	Thu 2/8/07	Wed 2/21/07	11
13	Substantive Requirements Process	45 days	Thu 2/8/07	Wed 4/11/07	11
14	Preparation for Public Comment Period	15 days	Thu 2/8/07	Wed 2/28/07	11
15	Public Comment Period	20 days	Thu 5/3/07	Wed 5/30/07	41
16	Prepare Responsiveness Summary	10 days	Thu 5/31/07	Wed 6/13/07	15
17	Prepare 100% Design	15 days	Thu 5/31/07	Wed 6/20/07	15
18	Distribute 100% Design to Stakeholders	1 day	Thu 6/21/07	Thu 6/21/07	17
19	**Island Complex Contractor Procurement**	**41 days**	**Fri 6/22/07**	**Fri 8/17/07**	
20	Develop RFP	10 days	Fri 6/22/07	Thu 7/5/07	18
21	RFP Submittal Period	15 days	Fri 7/6/07	Thu 7/26/07	20
22	Evaluate Contractor Proposals	10 days	Fri 7/27/07	Thu 8/9/07	21
23	Preliminary Selection of Contractor	2 days	Fri 8/10/07	Mon 8/13/07	22
24	Meet with Selected Contractor	1 day	Tue 8/14/07	Tue 8/14/07	23
25	Final Selection of Contractor or Re-evaluate Options	3 days	Wed 8/15/07	Fri 8/17/07	24
26	**Island Complex Remedial Action**	**45 days**	**Mon 8/20/07**	**Fri 10/19/07**	
27	Pre-construction Contractor Submittals	20 days	Mon 8/20/07	Fri 9/14/07	25
28	Remedial Action	25 days	Mon 9/17/07	Fri 10/19/07	27
29	**Murray Road Remedial Design and Remedial Action**	**218 days**	**Wed 12/20/06**	**Fri 10/19/07**	
30	**Murray Road Remedial Design**	**132 days**	**Wed 12/20/06**	**Thu 6/21/07**	
31	Murray Road Conceptual Design Review	2 days	Wed 12/20/06	Thu 12/21/06	
32	Topo Survey Field Work	3 days	Mon 1/22/07	Wed 1/24/07	
33	Draft Topo Survey	10 days	Thu 1/25/07	Wed 2/7/07	32
34	Final Topo Survey	5 days	Thu 2/8/07	Wed 2/14/07	33
35	Submit 30% Design Package	10 days	Thu 2/15/07	Wed 2/28/07	34
36	Review of 30% Design Package	10 days	Thu 3/1/07	Wed 3/14/07	35
37	Prepare Draft 90% Design Package	15 days	Thu 3/15/07	Wed 4/4/07	36
38	Review & Comment - 90% Design Package	10 days	Thu 4/5/07	Wed 4/18/07	37
39	Prepare Final 90% Design Package	10 days	Thu 4/19/07	Wed 5/2/07	38
40	Substantive Requirements Process	45 days	Thu 4/19/07	Wed 6/20/07	38
	Preparation for Public Comment Period	10 days	Thu 4/19/07	Wed 5/2/07	38
	Public Comment Period	20 days	Thu 5/3/07	Wed 5/30/07	41
43	Prepare Responsiveness Summary	10 days	Thu 5/31/07	Wed 6/13/07	42
44	Prepare 100% Design	15 days	Thu 5/31/07	Wed 6/20/07	42
45	Distribute 100% Design to Stakeholders	1 day	Thu 6/21/07	Thu 6/21/07	44
46	**Murray Road Contractor Procurement**	**41 days**	**Fri 6/22/07**	**Fri 8/17/07**	
47	Develop RFP	10 days	Fri 6/22/07	Thu 7/5/07	45
48	RFP Submittal Period	15 days	Fri 7/6/07	Thu 7/26/07	47
49	Evaluate Contractor Proposals	10 days	Fri 7/27/07	Thu 8/9/07	48
50	Preliminary Selection of Contractor	2 days	Fri 8/10/07	Mon 8/13/07	49
51	Meet with Selected Contractor	1 day	Tue 8/14/07	Tue 8/14/07	50
52	Final Selection of Contractor or Re-evaluate Options	3 days	Wed 8/15/07	Fri 8/17/07	51
53	**Murray Road Remedial Action**	**45 days**	**Mon 8/20/07**	**Fri 10/19/07**	
54	Pre-construction Contractor Submittals	20 days	Mon 8/20/07	Fri 9/14/07	52
55	Remedial Action	25 days	Mon 9/17/07	Fri 10/19/07	54
56	**Harvard Road North Remedial Design and Remedial Action**	**312 days**	**Thu 7/26/07**	**Fri 10/3/08**	
57	**Harvard Road North Remedial Design**	**191 days**	**Thu 7/26/07**	**Thu 4/17/08**	
58	Submit 30% Design Package	30 days	Thu 7/26/07	Wed 9/5/07	39FS+60 days
59	Review of 30% Design Package	20 days	Thu 9/6/07	Wed 10/3/07	58
60	Prepare Draft 90% Design Package	30 days	Thu 10/4/07	Wed 11/14/07	59
61	Review & Comment - 90% Design Package	20 days	Thu 11/15/07	Wed 12/12/07	60
62	Prepare Final 90% Design Package	15 days	Thu 11/15/07	Wed 12/5/07	60
63	Substantive Requirements Process	45 days	Thu 11/15/07	Wed 1/16/08	60
64	Preparation for Public Comment Period	15 days	Thu 1/17/08	Wed 2/6/08	63
65	Public Comment Period	20 days	Thu 2/7/08	Wed 3/5/08	64
66	Prepare Responsiveness Summary	15 days	Thu 3/6/08	Wed 3/26/08	65
67	Prepare 100% Design	15 days	Thu 3/27/08	Wed 4/16/08	66
68	Distribute 100% Design to Stakeholders	1 day	Thu 4/17/08	Thu 4/17/08	67
69	**Harvard Road North Contractor Procurement**	**71 days**	**Fri 4/18/08**	**Fri 7/25/08**	
70	Develop RFP	20 days	Fri 4/18/08	Thu 5/15/08	68
71	RFP Submittal Period	20 days	Fri 5/16/08	Thu 6/12/08	70
72	Evaluate Contractor Proposals	15 days	Fri 6/13/08	Thu 7/3/08	71
73	Preliminary Selection of Contractor	5 days	Fri 7/4/08	Thu 7/10/08	72
74	Meet with Selected Contractor	1 day	Fri 7/11/08	Fri 7/11/08	73
	Final Selection of Contractor or Re-evaluate Options	10 days	Mon 7/14/08	Fri 7/25/08	74
	Harvard Road North Remedial Action	**55 days**	**Mon 7/28/08**	**Fri 10/3/08**	
	Pre-construction Contractor Submittals	30 days	Mon 7/28/08	Fri 9/5/08	75
78	Remedial Action	20 days	Mon 9/8/08	Fri 10/3/08	77

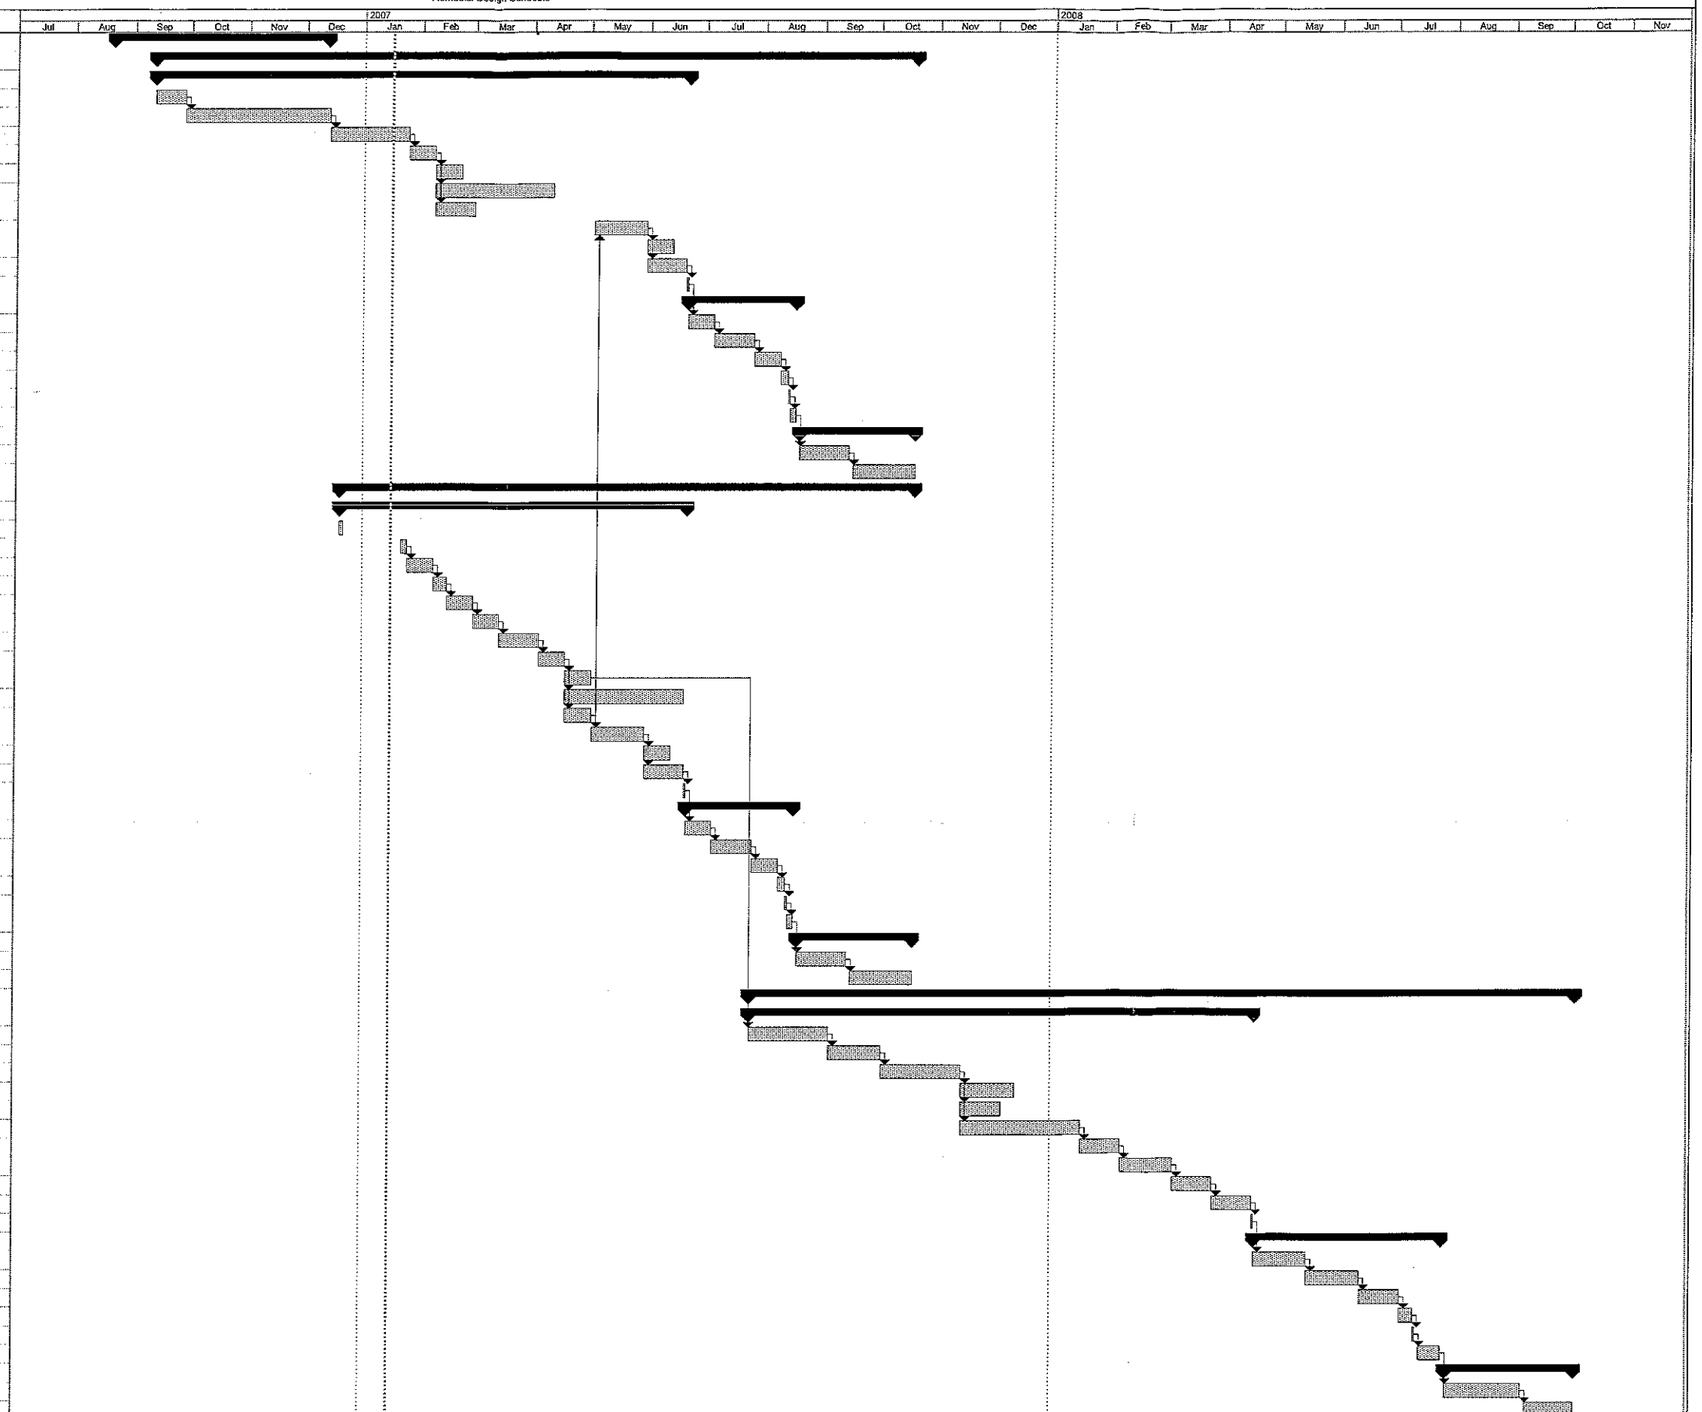

Project: IC RD schedule
Lat Updated: Tue 1/16/07

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
