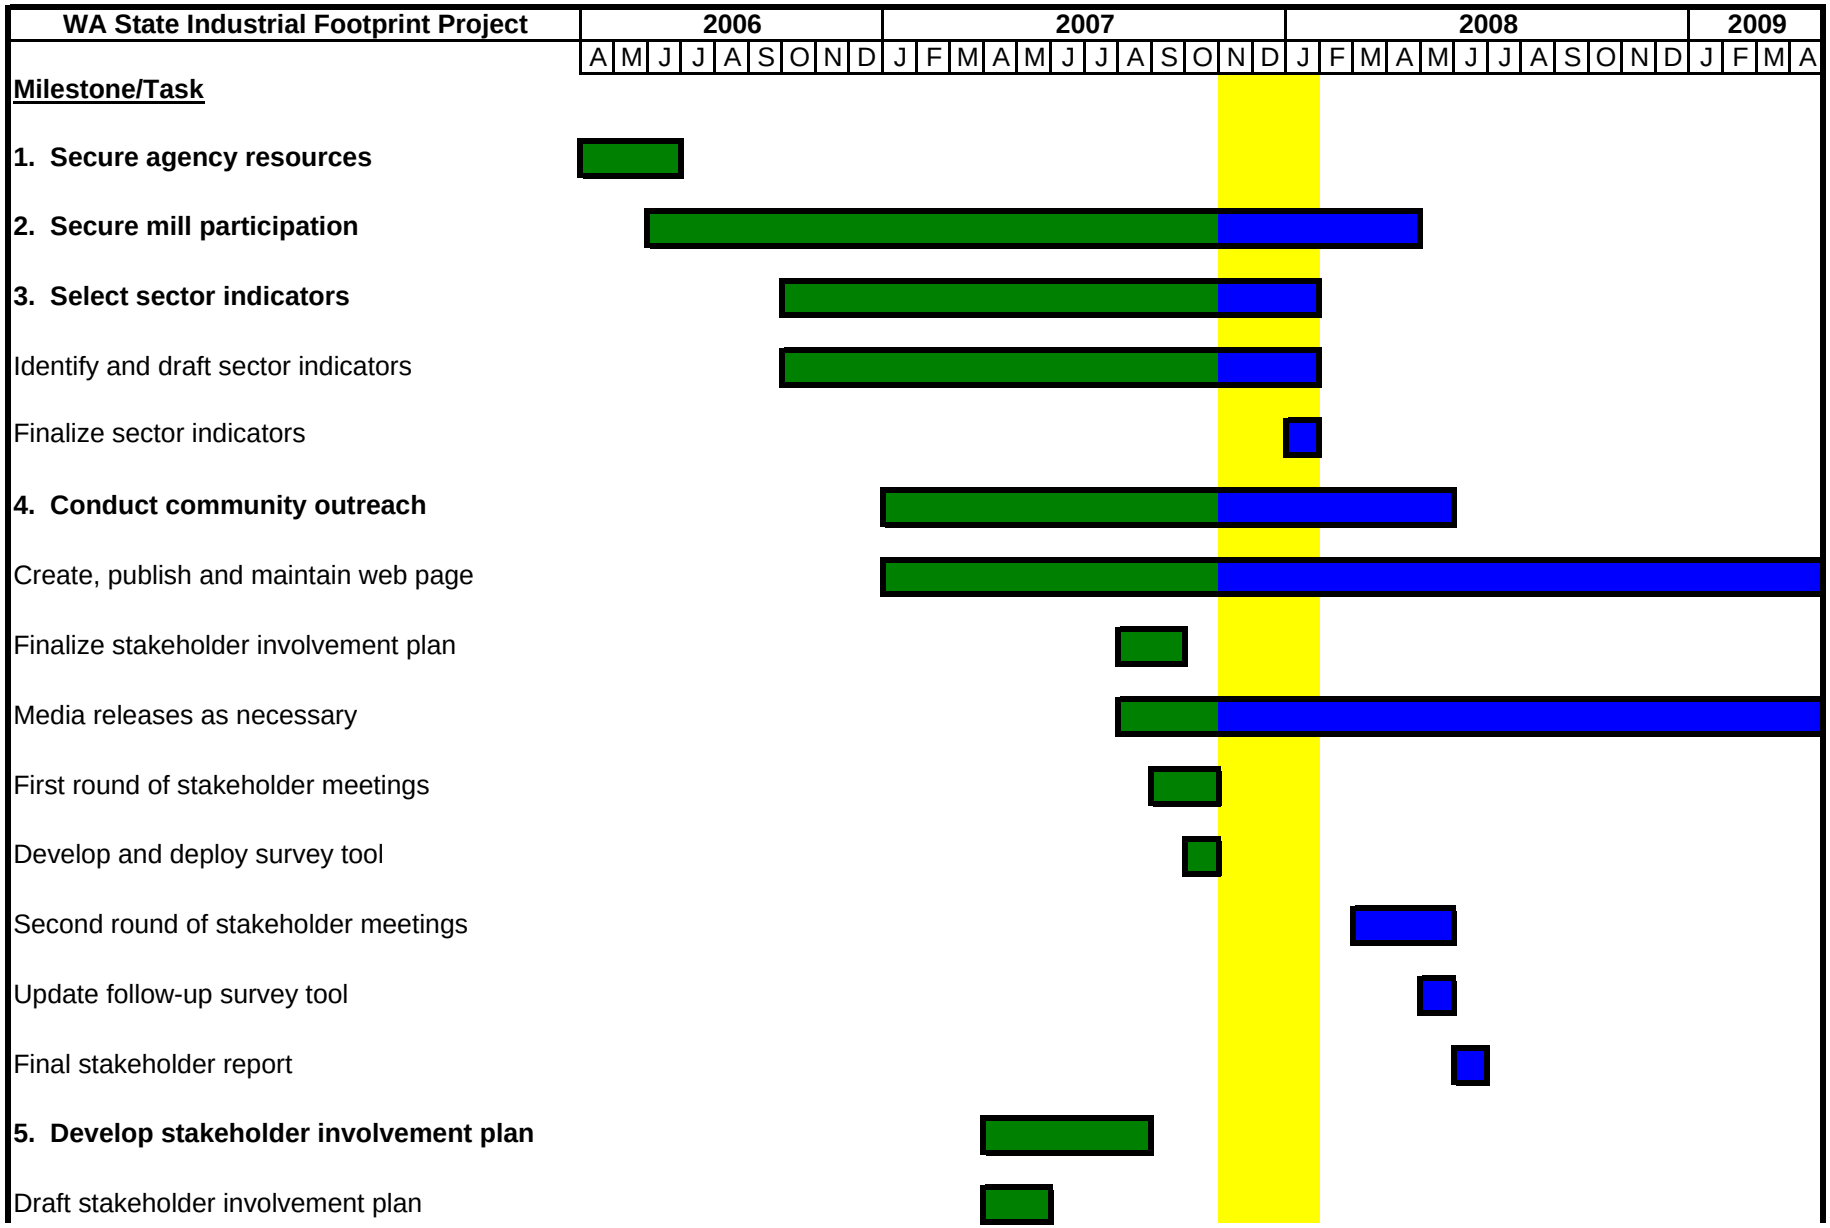
WA State Industrial Footprint Project
2006
2007
2008
2009
A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A
Milestone/Task
1. Secure agency resources
2. Secure mill participation
3. Select sector indicators
Identify and draft sector indicators
Finalize sector indicators
4. Conduct community outreach
Create, publish and maintain web page
Finalize stakeholder involvement plan
Media releases as necessary
First round of stakeholder meetings
Develop and deploy survey tool
Second round of stakeholder meetings
Update follow-up survey tool
Final stakeholder report
5. Develop stakeholder involvement plan
Draft stakeholder involvement plan

Finalize stakeholder involvement plan

6. Secure contractor support

Draft, finalize, and advertise the RFP

Hold interviews

Negotiate, finalize and sign contract

7. Select indicators for 8 mills

8. Amend QAPP

9. Develop baseline footprints

Collect data

Contractor recommendations

Spreadsheet tool for calculation developed

Baseline footprints complete

10. Develop sector baseline footprint

Collect data

Contractor recommendations

Spreadsheet tool for calculation developed

Sector footprint complete

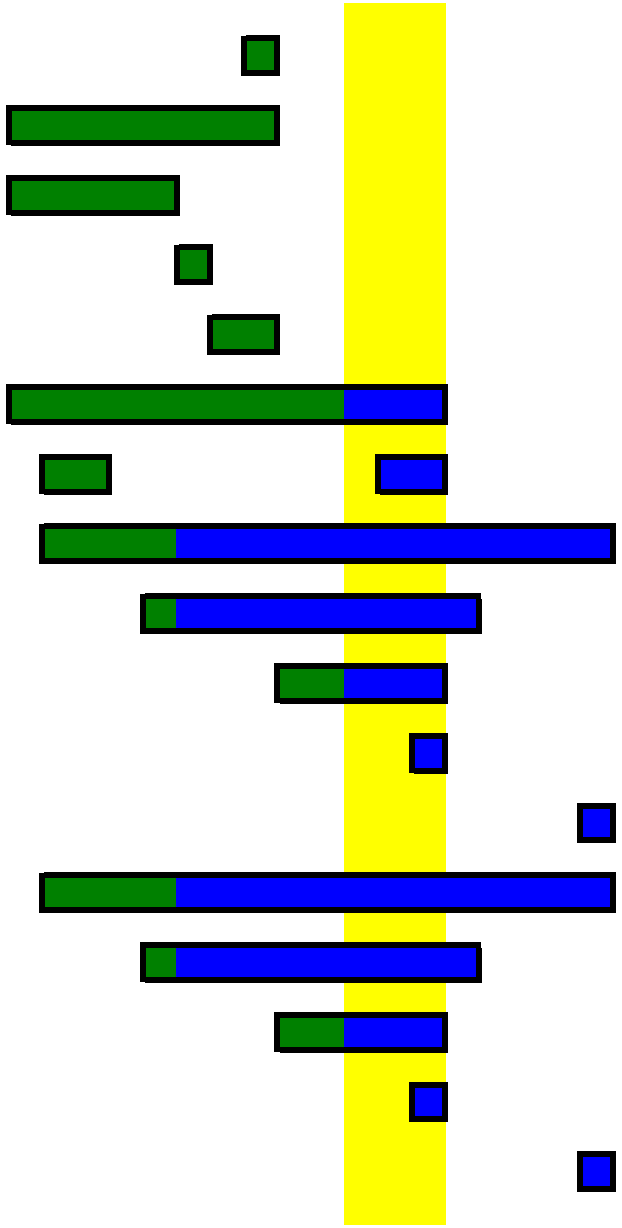

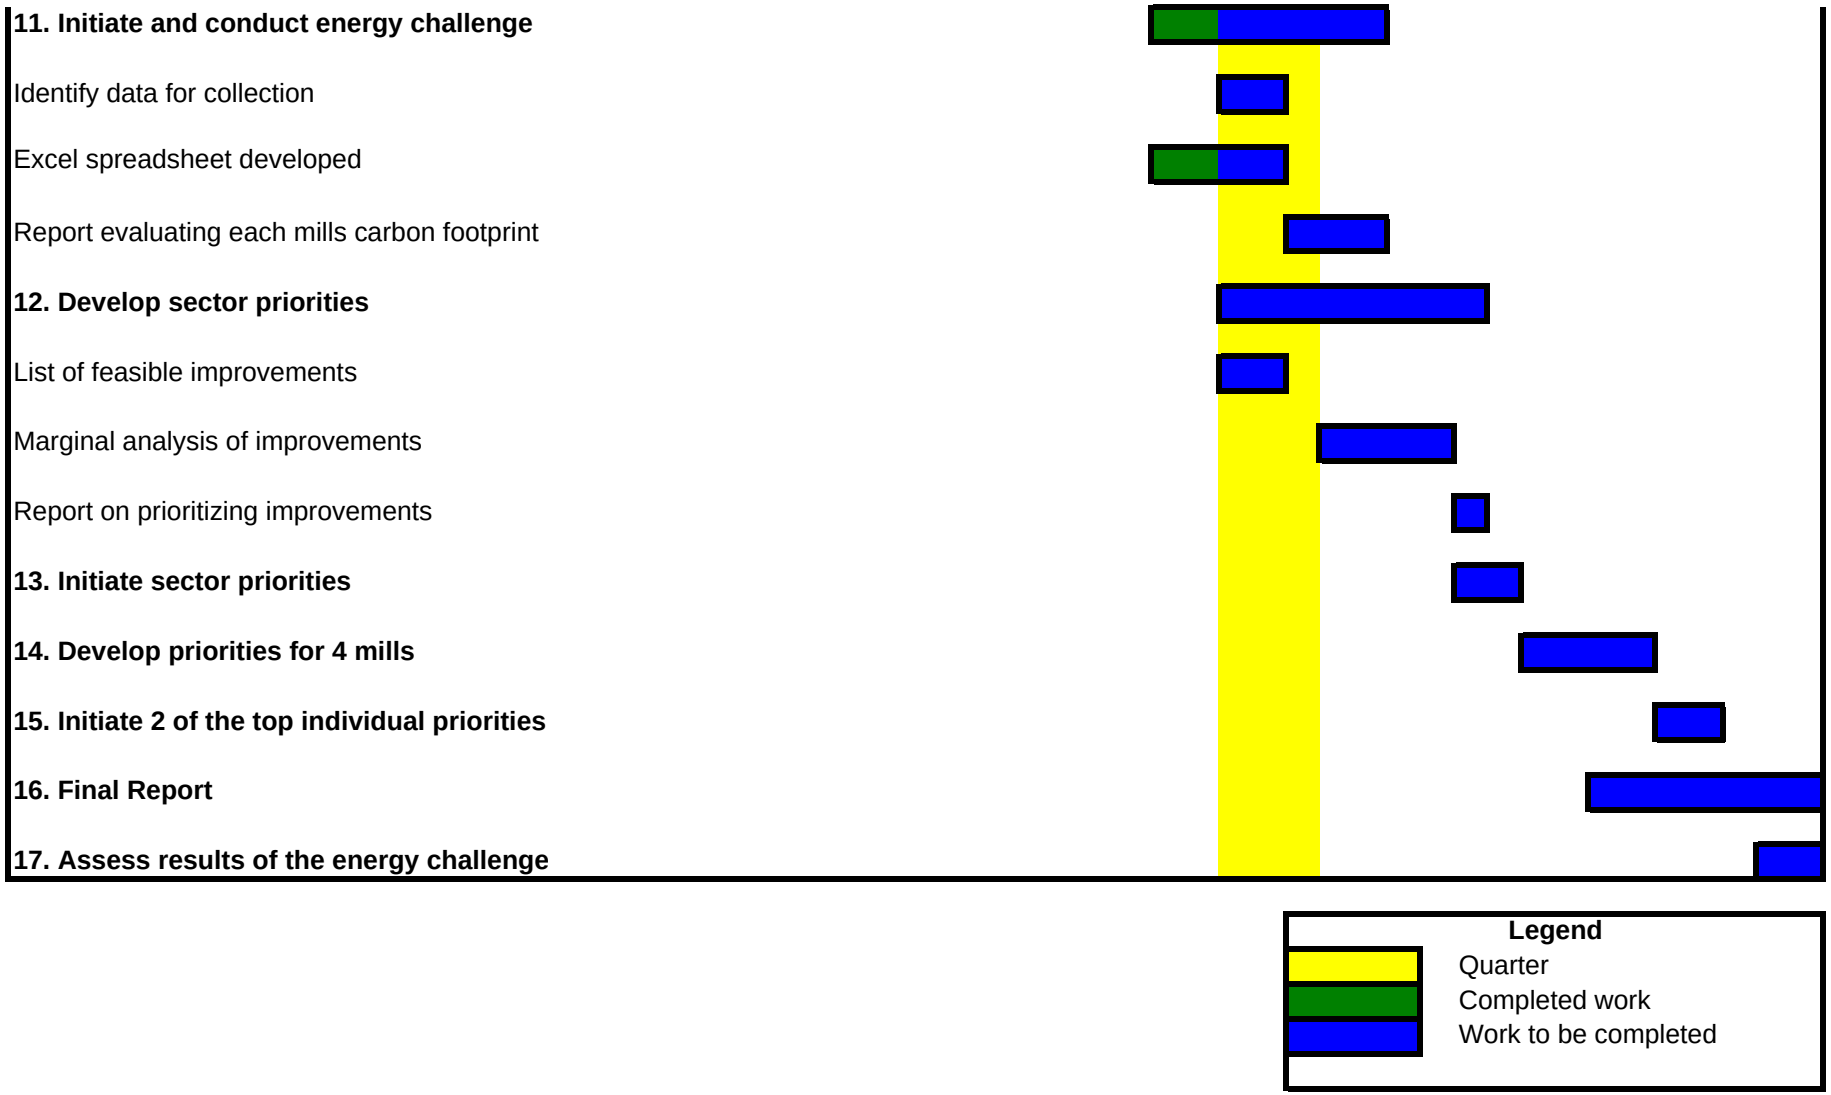
11. Initiate and conduct energy challenge
Identify data for collection
Excel spreadsheet developed
Report evaluating each mills carbon footprint
12. Develop sector priorities
List of feasible improvements
Marginal analysis of improvements
Report on prioritizing improvements
13. Initiate sector priorities
14. Develop priorities for 4 mills
15. Initiate 2 of the top individual priorities
16. Final Report
17. Assess results of the energy challenge
Legend
Quarter
Completed work
Work to be completed
