Dungeness Rulemaking Schedule 2008-2009

ID	Task Name	Duration	Start	Finish
1	**Stream Flow Calculations**	**50 days**	**Fri 3/28/08**	**Thu 6/5/08**
2	**Dungeness**	**50 days**	**Fri 3/28/08**	**Thu 6/5/08**
3	November through March 575 cfs	0 days	Fri 3/28/08	Fri 3/28/08
4	April through July 475 cfs	0 days	Fri 3/28/08	Fri 3/28/08
5	August through October 180 cfs	0 days	Fri 3/28/08	Fri 3/28/08
6	smooth out the curves	20 days	Fri 3/28/08	Thu 4/24/08
7	Seasonal closure discussion--start and stop dates	30 days	Fri 4/25/08	Thu 6/5/08
8	determination of dates of seasonal closure	0 days	Thu 6/5/08	Thu 6/5/08
9	**Small Streams**	**50 days**	**Fri 3/28/08**	**Thu 6/5/08**
10	cfs flows	0 days	Fri 3/28/08	Fri 3/28/08
11	smooth out the curves	20 days	Fri 3/28/08	Thu 4/24/08
12	Seasonal closure discussion--start and stop dates	30 days	Fri 4/25/08	Thu 6/5/08
13	determination of dates of seasonal closure	0 days	Thu 6/5/08	Thu 6/5/08
14	**High Flow possible diversion limits**	**117 days**	**Fri 3/28/08**	**Mon 9/8/08**
15	**Modeling**	**87 days**	**Fri 3/28/08**	**Mon 7/28/08**
16	first set of scenarios	67 days	Fri 3/28/08	Mon 6/30/08
17	TAG meeting	6 days	Tue 7/1/08	Tue 7/8/08
18	discussions regarding implications	14 days	Wed 7/9/08	Mon 7/28/08
19	Preliminary agreement on high flow diversion window	0 days	Mon 7/28/08	Mon 7/28/08
20	discussion of high flow diversion with DREC and DWWG	20 days	Tue 7/29/08	Mon 8/25/08
21	final diversion window/upper flow allocation	10 days	Tue 8/26/08	Mon 9/8/08
22	**Water Exchange Discussion**	**275 days**	**Fri 3/28/08**	**Thu 4/16/09**
23	**Ecology is hiring a consultant to help structure the exchange**	**50 days**	**Fri 3/28/08**	**Thu 6/5/08**
24	RFP on street	20 days	Fri 3/28/08	Thu 4/24/08
25	Consultants provide proposals	15 days	Fri 4/25/08	Thu 5/15/08
26	Ecology/County evaluate proposals	5 days	Fri 5/16/08	Thu 5/22/08
27	Interviews	5 days	Fri 5/23/08	Thu 5/29/08
28	Contract negotiations	5 days	Fri 5/30/08	Thu 6/5/08
29	**Framework**	**225 days**	**Fri 6/6/08**	**Thu 4/16/09**
30	contractor provides preliminary framework	15 days	Fri 6/6/08	Thu 6/26/08
31	discussion with exec and working groups	20 days	Fri 6/27/08	Thu 7/24/08

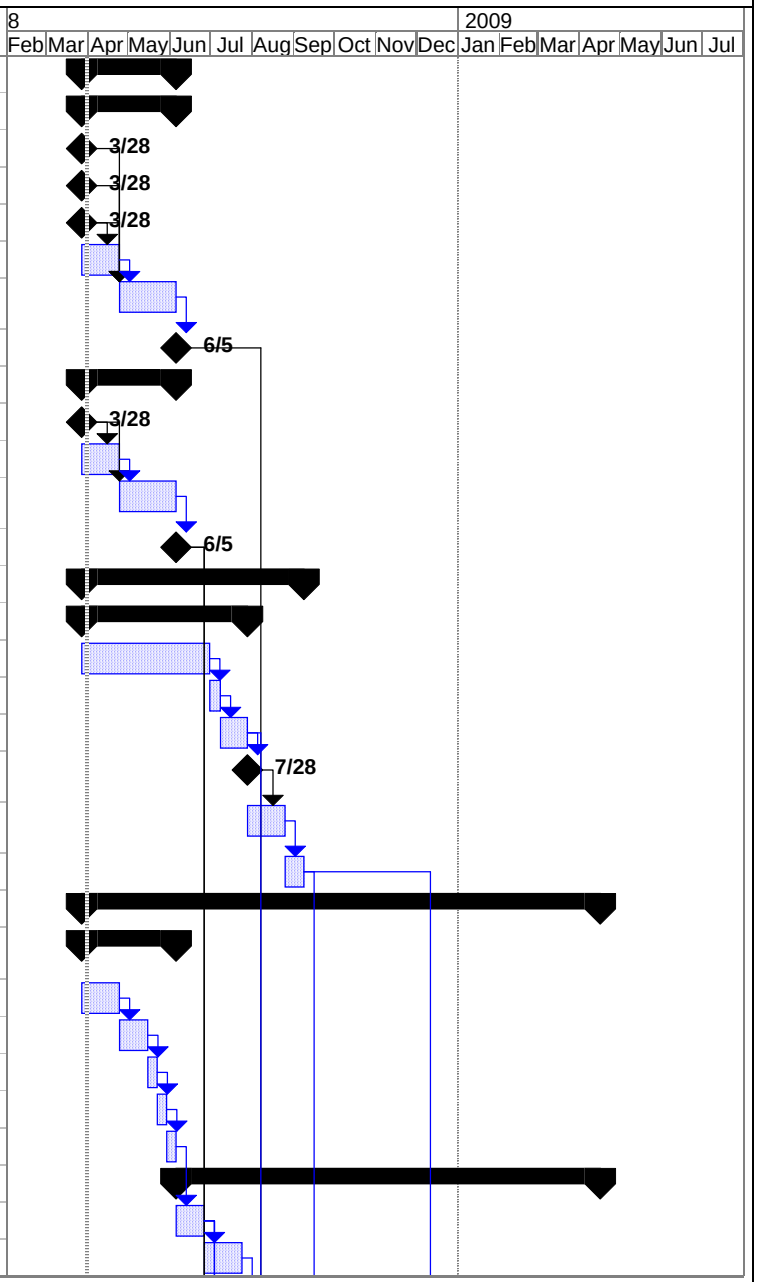

printed Mon 3/31/08

Dungeness Rulemaking Schedule 2008-2009

ID	Task Name	Duration	Start	Finish
32	contractor refines framework, provides statuory language	10 days	Fri 7/25/08	Thu 8/7/08
33	administration, funding, water, options in language	40 days	Fri 8/8/08	Thu 10/2/08
34	more discussion	30 days	Fri 10/3/08	Thu 11/13/08
35	final structure	20 days	Fri 11/14/08	Thu 12/11/08
36	wet water acquisition	90 days	Fri 12/12/08	Thu 4/16/09
37	water bank in place and wet	0 days	Thu 4/16/09	Thu 4/16/09
38	**Guidance document (here's what mitigation would look like)**	**119 days**	**Fri 6/27/08**	**Wed 12/10/08**
39	draft of guidance document (DOE)	20 days	Fri 6/27/08	Thu 7/24/08
40	discussion of guidance document (DREC, DWWG)	22 days	Fri 7/25/08	Mon 8/25/08
41	next draft of guidance document (DOE)	15 days	Tue 8/26/08	Mon 9/15/08
42	another round of discussion of draft document (DREC, DWWG)	22 days	Tue 9/16/08	Wed 10/15/08
43	final draft of guidance document (DOE)	10 days	Thu 10/16/08	Wed 10/29/08
44	legal review of guidance document (AG)	20 days	Thu 10/30/08	Wed 11/26/08
45	revise guidance document	10 days	Thu 11/27/08	Wed 12/10/08
46	final "draft" guidance document	0 days	Wed 12/10/08	Wed 12/10/08
47				
48	**MOU with County**	**207 days**	**Fri 6/27/08**	**Mon 4/13/09**
49	draft of MOU, including plan review	20 days	Fri 6/27/08	Thu 7/24/08
50	discussion of MOU	22 days	Fri 7/25/08	Mon 8/25/08
51	next draft of MOU	15 days	Tue 8/26/08	Mon 9/15/08
52	another round of discussion of draft MOU	22 days	Tue 9/16/08	Wed 10/15/08
53	final draft of MOU	10 days	Fri 12/12/08	Thu 12/25/08
54	legal review of MOU	20 days	Fri 12/26/08	Thu 1/22/09
55	revise MOU	15 days	Fri 1/23/09	Thu 2/12/09
56	review of MOU with DREC and DWWG	22 days	Fri 2/13/09	Mon 3/16/09
57	final MOU with County	10 days	Tue 3/17/09	Mon 3/30/09
58	County Commissioners approve	10 days	Tue 3/31/09	Mon 4/13/09
59	DOE approve	10 days	Tue 3/31/09	Mon 4/13/09
60	**Rule finalizing**	**40 days**	**Fri 8/8/08**	**Thu 10/2/08**
61	Sarah completes draft	5 days	Fri 8/8/08	Thu 8/14/08
62	Exec and working group review	15 days	Fri 8/15/08	Thu 9/4/08
63	Workshop	10 days	Fri 9/5/08	Thu 9/18/08

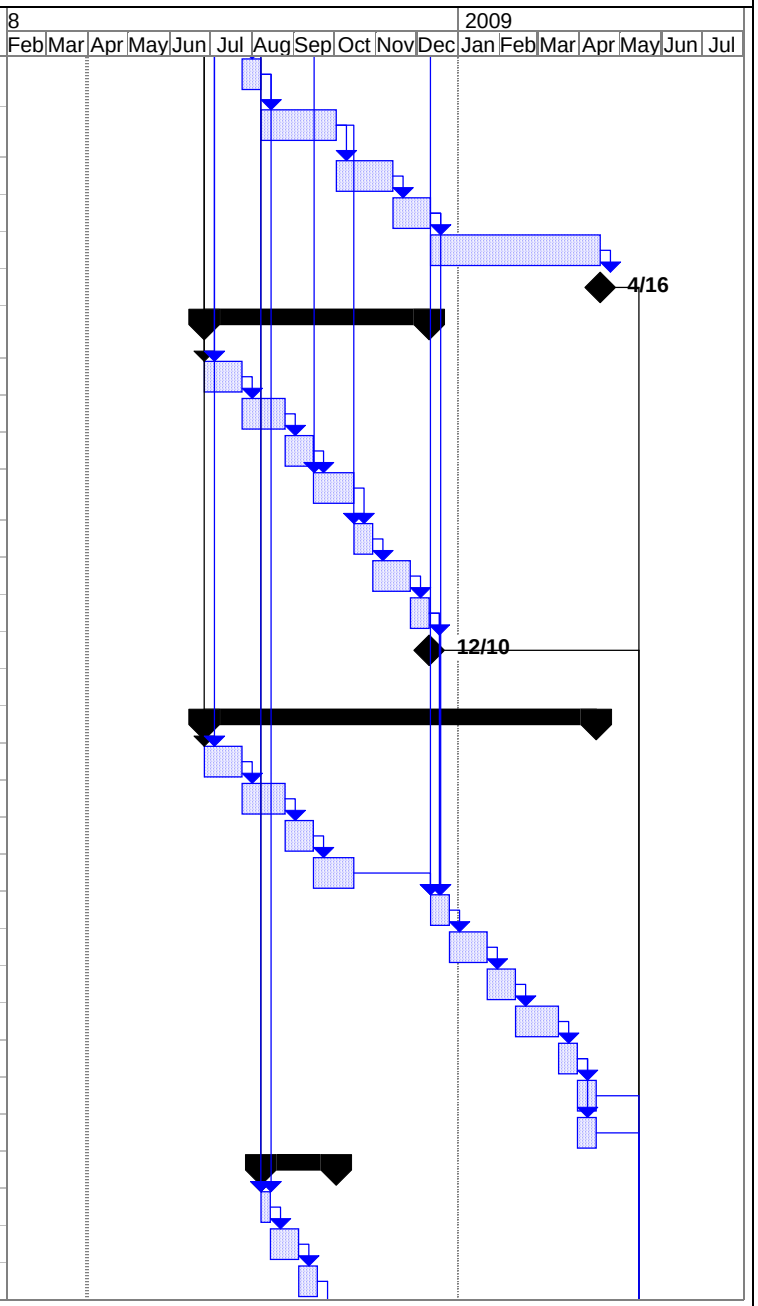

Dungeness Rulemaking Schedule 2008-2009
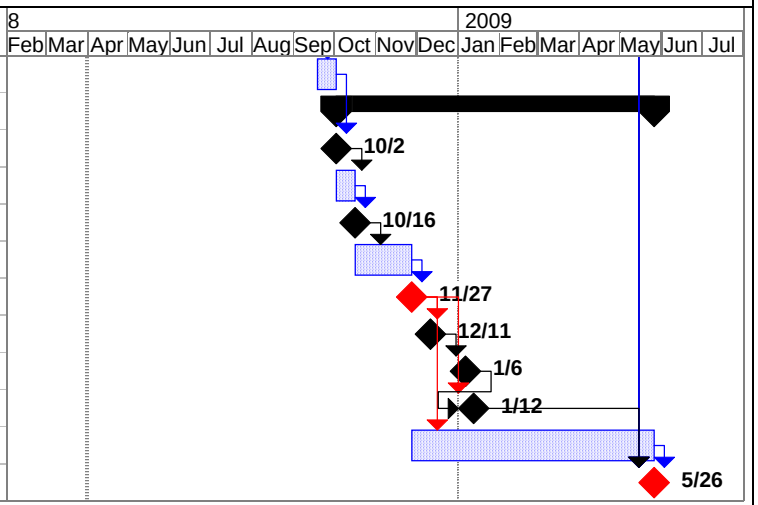
ID	Task Name	Duration	Start	Finish
64	revise final rule	10 days	Fri 9/19/08	Thu 10/2/08
65	**Rule review and fililng**	**168 days**	**Thu 10/2/08**	**Tue 5/26/09**
66	final rule to AG	0 days	Thu 10/2/08	Thu 10/2/08
67	AG review	10 days	Fri 10/3/08	Thu 10/16/08
68	final rule to internal review	0 days	Thu 10/16/08	Thu 10/16/08
69	economic and SEPA review	6 wks	Fri 10/17/08	Thu 11/27/08
70	**file with code reviser**	**0 days**	**Thu 11/27/08**	**Thu 11/27/08**
71	public workshop	0 days	Thu 12/11/08	Thu 12/11/08
72	public hearing (3 weeks minimum)	0 days	Tue 1/6/09	Tue 1/6/09
73	close public comment period	0 days	Mon 1/12/09	Mon 1/12/09
74	administrative time clock	180 edays	Thu 11/27/08	Tue 5/26/09
75	**rule final**	**0 days**	**Tue 5/26/09**	**Tue 5/26/09**
